

40060

4:00 10:00

LINCOLN COUNTY HEALTH DEPARTMENT

302 NORTH ACADEMY STREET • LINCOLNTON, N.C. 28092 • (704) 736-8426

Application Type: EH IMPROVEMENT APPLICATION

Date: 10/25/02

Permit #: 02-90000639 PIN: 2664 -00 -83 -6231

Parcel ID: 80777

Owner: SMITH, STEVEN & JANA (704) 748-2296

864 MICKEY RD LINCOLNTON NC 28092

Applicant: PIEDMONT DEVELOPMENT (704) 736-4330

DANIEL LOVETT/ AGENT 2671 E MAIN ST LINCOLNTON NC 28092

Directions to property: \*UNASSIGNED

HWY 27W TO REEPSVILLE RD, TURN ON STARTOWN RD, TURN R ON MCREE RD, FOLLOW TO END

Residence: Y


Nbr of Bedrooms: 3

Water Supply: PRIVATE

IMPROVEMENT PERMIT

REPAIR

LOT DENIED

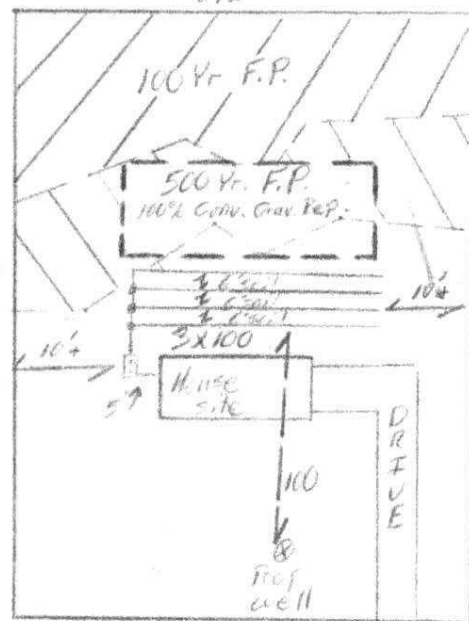


use Boxes only. No "T" in header ditch.

4 lines 3x100 12" stone

FINAL COMPLETION

OP

RC

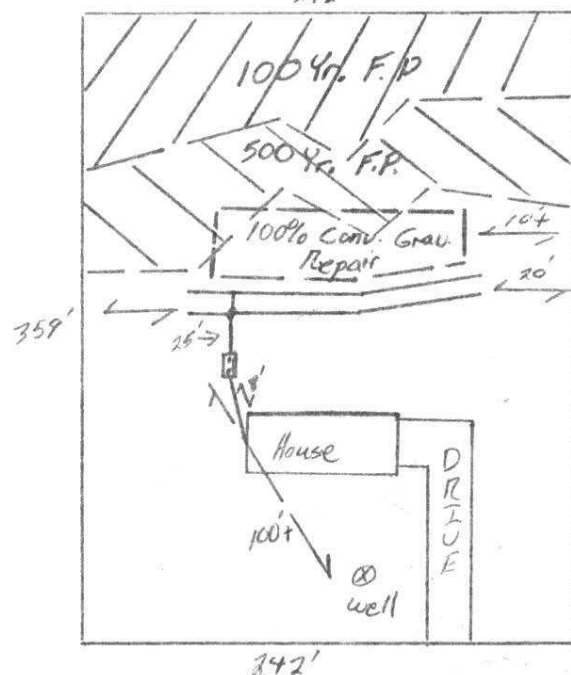

changed to 350' see Attached Warranty

AUTHORIZATION TO CONSTRUCT

TYPE OF SYSTEM Conv. Grav.

TANK SIZE 1000 gal

ABSORPTION AREA 1200 sq ft

TRENCH WIDTH & LENGTH 3x100

NUMBER OF TRENCHES 4

TRENCH SPACING 9 OC

GRAVEL DEPTH 12"

DISTANCE TO WATER SUPPLY 100' FT.

DESIGN FLOW 360 gpd. LTAR 3

CONDITIONS Stay 10ft off all property lines

Install lines on contour. Provide tank w/ filter & marker

HEALTH DEPT. REP. [Signature]

DATE: 10.25.2002

TANK MANUFACTURER GM - STB-354 12.21.01

TANK SIZE 1000 gal

ABSORPTION AREA 780 sq ft

TRENCH WIDTH & LENGTH 3x130

NUMBER OF TRENCHES 2

GRAVEL DEPTH N/A Chamber

DISTANCE TO WATER SUPPLY 100+ FT.

INSTALLER Gary Miller

CONDITIONS system is 10ft off all property lines

Lines installed on contour. Tank provided w/ filter & marker

HEALTH DEPT. REP. [Signature]

DATE: 1.22.03

IMPROVEMENT PERMIT: THIS IMPROVEMENT PERMIT IS SUBJECT TO REVOCATION IF SITE PLANS OR THE INTENDED USE ARE CHANGED FROM THOSE SHOWN ON PERMIT. CHANGES FROM THE ABOVE PERMIT REQUIRE HEALTH DEPARTMENT APPROVAL. INSTALLER SHALL BE REQUIRED TO HAVE AN "AUTHORIZATION TO CONSTRUCT" (VALID FOR 60 MONTHS) BEFORE INSTALLING THE ABOVE SYSTEM.

FINAL COMPLETION: FINAL APPROVAL OF THIS SYSTEM SHALL INDICATE THAT THE SYSTEM HAS BEEN INSTALLED IN ACCORDANCE WITH STATE REGULATIONS, BUT IN NO WAY SHOULD BE TAKEN AS A GUARANTEE THAT THE SYSTEM WILL FUNCTION SATISFACTORY FOR ANY GIVEN TIME.

2 130' 130' 390' 390' 780'
